



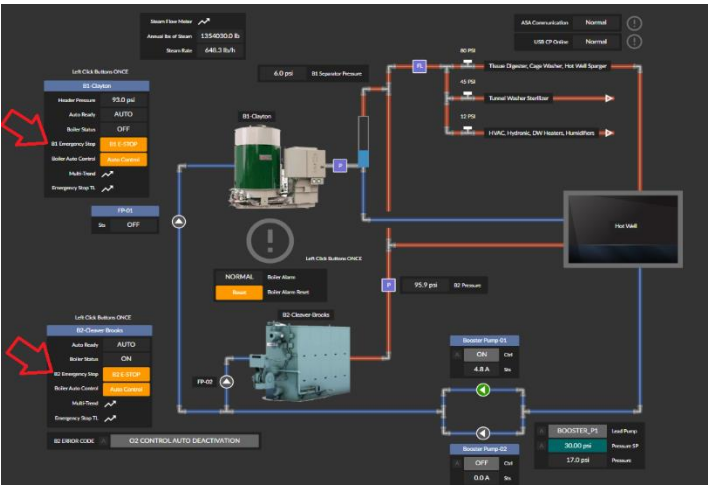
Procedure #4

Prepared by:
Andy Gomes**Approved by:**
Clive Baek**Review Date:** March 2026**Original Date:** October 2018

CCM STEAM PLANT EMERGENCY REMOTE STOP PROCEDURE

Remote stop testing of the CCM Steam Plant Boiler plants is to ensure that the Steam plants will shut down safely when needed if there is an emergency.

The CCM shutdown will take place on Wednesday afternoons after 2pm

Step	Operation	Initial when Complete	Date and Time Completed
1	The CCM Operating Engineer will contact the Operations Centre. The CCM Engineer will and ask the Operations Centre Engineer to remotely stop the Steam boiler that is operating.		
2	The Operations Centre Engineer will shut down the boiler by pressing the EMERGENCY STOP button on the DDC screen for the corresponding boiler. This is done by pressing the left mouse button when the cursor is over the Emergency Stop button.		
3	There is an EMERGENCY STOP button for each of the two Steam boilers as outlined in the diagram below. 		

4	CCM Operating Engineer to confirm that the corresponding boiler has remotely stopped. (maximum time from button press to the boiler physically shutting down is not to exceed one minute.		
5	Operations Centre Engineer will release the EMERGENCY STOP button. This is done by pressing the left mouse button when the cursor is over the MASTER AUTO CONTROL button. The button should return to its original green outline.		
6	The CCM Operating Engineer to reset the boiler local alarms and restart the corresponding boiler.		
7	CCM Operating Engineer and Operations Centre Engineer will make appropriate log book entry.		

This is the end of the procedure.
